

North Stonington Emergency Services Building - Field Report #1 - 7-21-17-7-28-17

Prepared by Michael Faenza

Description

This field report contains observations from site activities performed during the week of July 21, 2017 and July 28, 2017.

The purpose of this report is to document the progress of the project.

Subcontractors working on site this week:

Suchocki & Son Inc. - Sitework
CE Electric - Electrical

Key Activities this week include:

Delivery of Project Trailer - Complete
Installation of Site Fencing - Complete
Installation of USDA & DECD Signage - Complete
Surveying and Layout of Site - In Progress
Installation of Temporary Electric Service - Complete
Site Grading - In Progress
Excavation for Building Footings - In Progress
Removal of Stone Stockpile - Complete
Screening of Top Soil Stockpile - Complete

Please see individual photos and locations within the report for specific detail of activities performed.

Contents


#8 July 21st	3
#9 July 21st	4
#10 July 21st	4
#1 July 26th	5
#2 July 26th	6
#3 July 26th	7
#4 July 26th	8

North Stonington Emergency Services Building

#5 July 28th	9
#6 July 28th	10
#7 July 28th	11

North Stonington Emergency Services Building

#8 July 21st

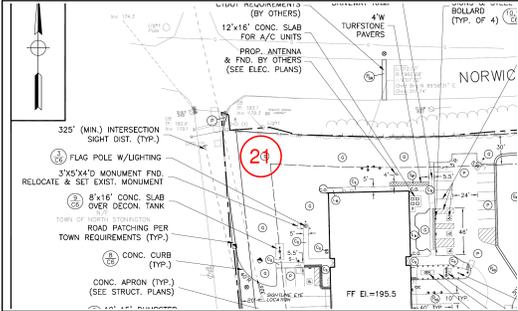

Sheet
C1

Status
Open

Created
Jul 28, 2017 at 2:52pm
mfaenza@crec.org

Last Updated
Jul 28, 2017 at 2:56pm

Description


USDA and DECD signs have been installed. Site fencing has been installed.

Photos



Jul 20, 2017 at 3:20pm

#9 July 21st

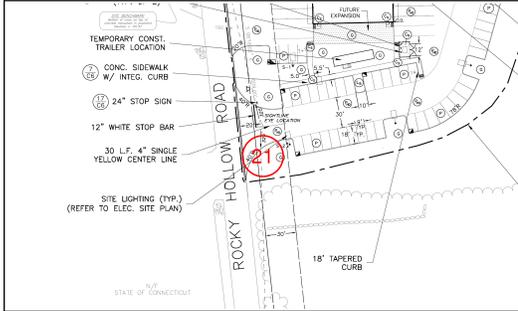

Sheet C1

Status Open

Created Jul 28, 2017 at 2:56pm mfaenza@crec.org

Last Updated Jul 28, 2017 at 2:57pm

Description


Temporary electric service has been installed.

Photos



Jul 28, 2017 at 2:56pm

#10 July 21st

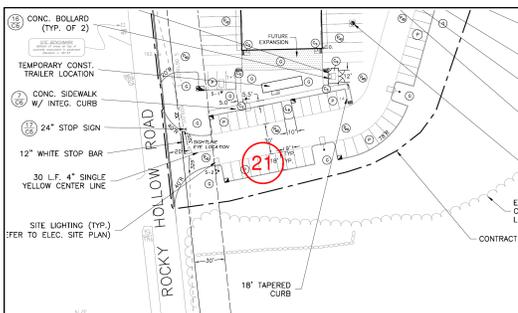

Sheet C1

Status Open

Created Jul 28, 2017 at 2:57pm mfaenza@crec.org

Last Updated Jul 28, 2017 at 2:57pm

Description

Project trailer has been delivered.


North Stonington Emergency Services Building

Photos



Jul 28, 2017 at 2:57pm

#1 July 26th

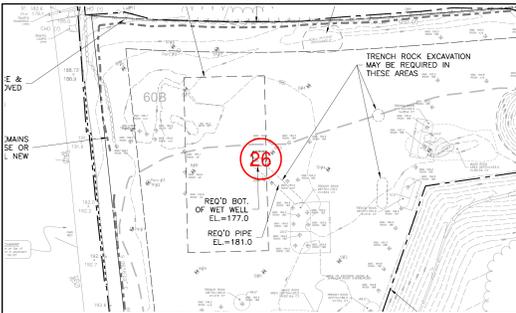

Sheet
C2

Status
Open

Created
Jul 26, 2017 at 9:50am
mfaenza@crec.org

Last Updated
Jul 26, 2017 at 9:50am

Description

Wet well has been staked out.


North Stonington Emergency Services Building

Photos



Jul 26, 2017 at 9:50am

#2 July 26th

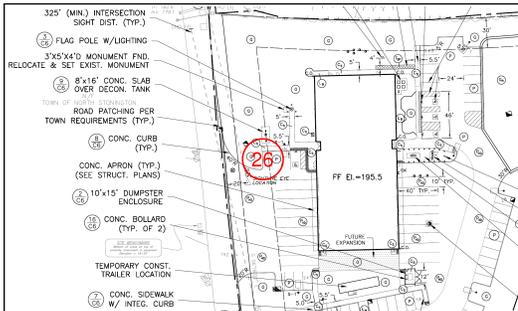

Sheet
C1

Status
Open

Created
Jul 26, 2017 at 9:53am
mfaenza@crec.org

Last Updated
Jul 26, 2017 at 9:59am

Description


Western side of site is being cut to grade.

Photos



Jul 26, 2017 at 9:53am

#3 July 26th

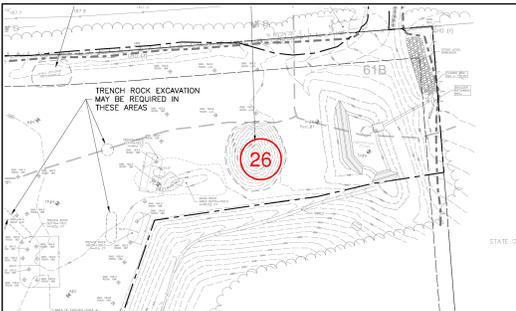

Sheet
C2

Status
Open

Created
Jul 26, 2017 at 9:59am
mfaenza@crec.org

Last Updated
Jul 26, 2017 at 10:55am

Description

Top soil stockpile has been screened.


North Stonington Emergency Services Building

Photos



Jul 26, 2017 at 10:00am

#4 July 26th

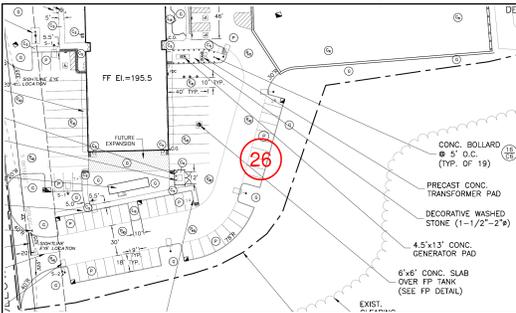

Sheet
C1

Status
Open

Created
Jul 26, 2017 at 12:58pm
mfaenza@crec.org

Last Updated
Jul 26, 2017 at 12:59pm

Description

Site is being cut to grade.


North Stonington Emergency Services Building

Photos



Jul 26, 2017 at 12:58pm

#5 July 28th

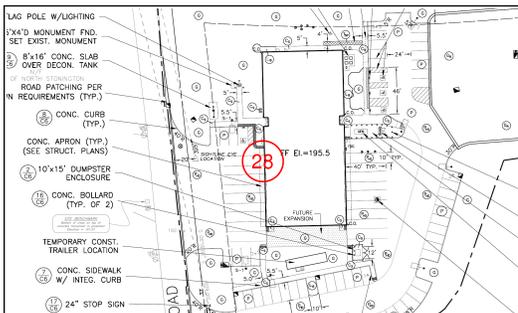

Sheet
C1

Status
Open

Created
Jul 28, 2017 at 1:59pm
mfaenza@crec.org

Last Updated
Jul 28, 2017 at 2:00pm

Description

Excavation for building footing has begun.


North Stonington Emergency Services Building

Photos



Jul 28, 2017 at 2:00pm

#6 July 28th

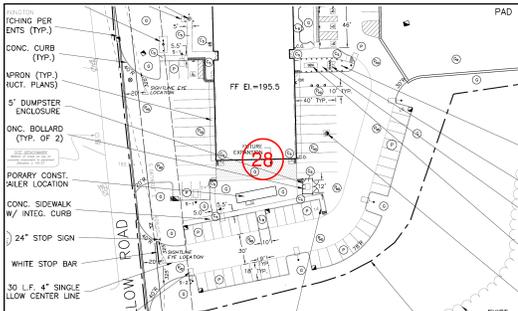

Sheet
C1

Status
Open

Created
Jul 28, 2017 at 2:00pm
mfaenza@crec.org

Last Updated
Jul 28, 2017 at 2:03pm

Description


Excavation for building footings has begun.

Photos



Jul 28, 2017 at 2:00pm

#7 July 28th

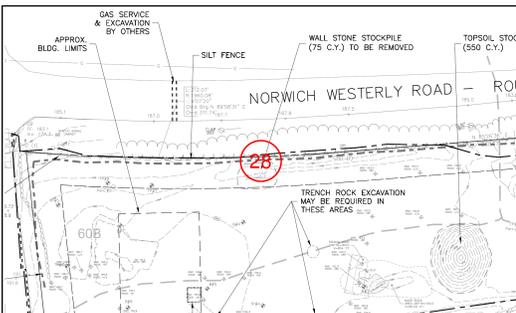

Sheet
C2

Status
Open

Created
Jul 28, 2017 at 2:03pm
mfaenza@crec.org

Last Updated
Jul 28, 2017 at 2:30pm

Description

Stone stockpile has nearly been completely removed.

Photos



Jul 28, 2017 at 2:04pm
