

North Stonington Center for Emergency Services - Field Report #11 - 10-9-17 - 10-13-17

Prepared by Michael Faenza

Description

This field report contains observations from site activities performed during the week of October 13, 2017.

The purpose of this report is to document the progress of the project.

Subcontractors working on site this week:

- Suchocki & Son Inc. - Sitework
- Black Dog Concrete - Concrete
- Main Enterprises - Plumbing
- CE Electrical - Electrical

Key Activities this week include:


- Backfill of Fire Protection Storage Tank - complete
- Forming and Pouring of Tie, Beams, Foundation Walls and Impact Walls - Complete
- Installation of Underslab Electrical Conduit - In Progress
- Backfilling of Building Interior Slabs - In Progress
- Installation of Oil / Water Separator and Holding Tank - Complete

Please see individual photos and locations within the report for specific detail of activities performed.

Contents

#99 October 13th	2
#98 October 13th	3
#96 October 13th	4
#95 October 13th	5
#94 October 13th	6
#93 October 13th	7
#92 October 11th	8
#91 October 11th	9
#90 October 11th	10

#99 October 13th

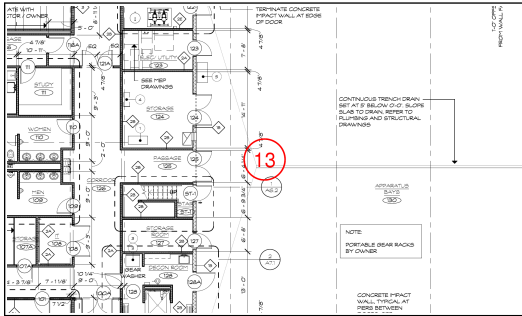

Sheet
A1.0

Status
Open

Created
Oct 13, 2017 at 2:09pm
gblackstone@crec.org

Last Updated
Oct 17, 2017 at 10:05am

Description

Trench drain installation is in progress in apparatus bay.

Photos



Oct 13, 2017 at 2:09pm




Oct 13, 2017 at 2:10pm



Oct 13, 2017 at 2:10pm

North Stonington Emergency Services Building

#98 October 13th

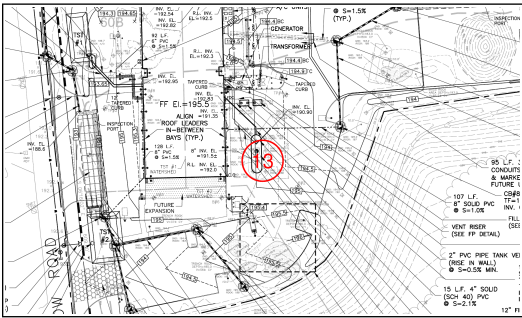

Sheet
C3

Status
Open

Created
Oct 13, 2017 at 2:08pm
gblackstone@crec.org

Last Updated
Oct 17, 2017 at 10:06am

Description

Fire Protection Storage Tank has been backfilled.


Photos



Oct 13, 2017 at 2:08pm

North Stonington Emergency Services Building

#96 October 13th

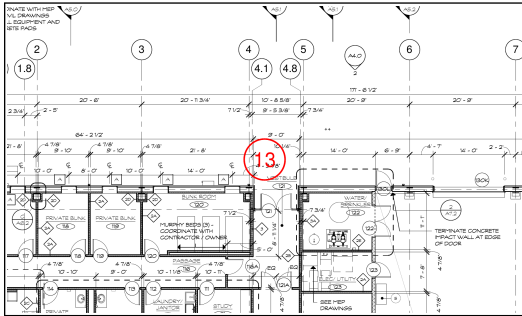

Sheet
A1.0

Status
Open

Created
Oct 13, 2017 at 2:06pm
gblackstone@crec.org

Last Updated
Oct 17, 2017 at 10:33am

Description

Electrical conduits for underslab electrical have been stubbed out of the building.

Photos




Oct 13, 2017 at 2:06pm



Oct 13, 2017 at 2:06pm

#95 October 13th

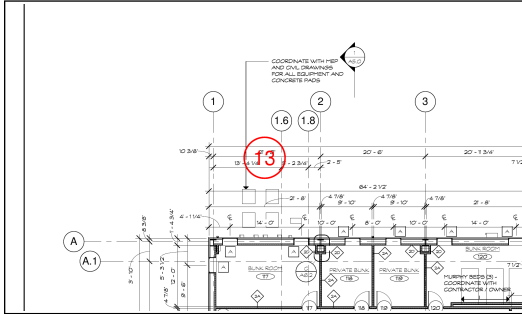

Sheet
A1.0

Status
Open

Created
Oct 13, 2017 at 2:03pm
gblackstone@crec.org

Last Updated
Oct 17, 2017 at 10:24am

Description

Roof leaders installation in progress.

Photos




Oct 13, 2017 at 2:03pm



Oct 13, 2017 at 2:03pm




Oct 13, 2017 at 2:03pm

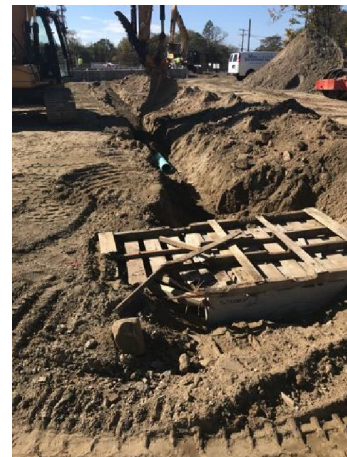

Oct 13, 2017 at 2:04pm

#94 October 13th

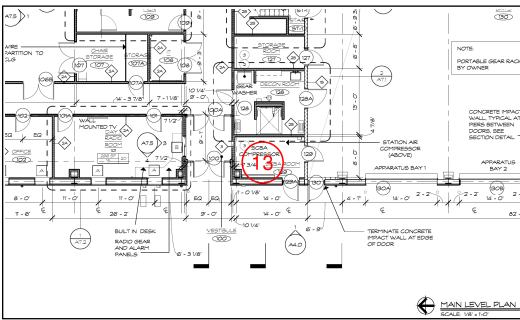

Sheet
A1.0

Status
Open

Created
Oct 13, 2017 at 2:00pm
gblackstone@crec.org

Last Updated
Oct 17, 2017 at 10:25am

Description

Rigid foam installation in progress underslab in administration area.

Photos



Oct 13, 2017 at 2:00pm




Oct 13, 2017 at 2:00pm

North Stonington Emergency Services Building



Oct 13, 2017 at 2:00pm

#93 October 13th

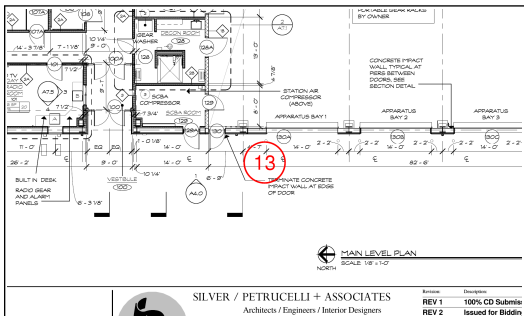

Sheet
A1.0

Status
Open

Created
Oct 13, 2017 at 1:59pm
gblackstone@crec.org

Last Updated
Oct 17, 2017 at 10:26am

Description

Underslab prep in progress at apparatus bay area.


North Stonington Emergency Services Building

Photos



Oct 13, 2017 at 1:59pm

#92 October 11th

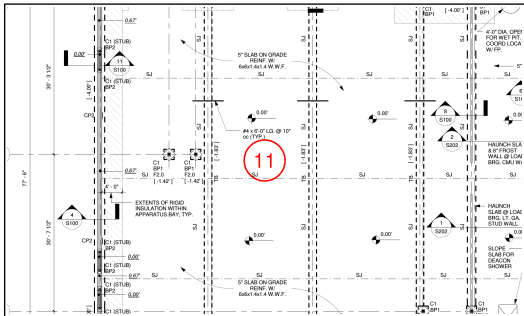

Sheet
S100

Status
Open

Created
Oct 11, 2017 at 4:15pm
mfaenza@crec.org

Last Updated
Oct 11, 2017 at 4:16pm

Description

Crushed stone base has been installed in administration area.


North Stonington Emergency Services Building

Photos



Oct 11, 2017 at 4:15pm

#91 October 11th

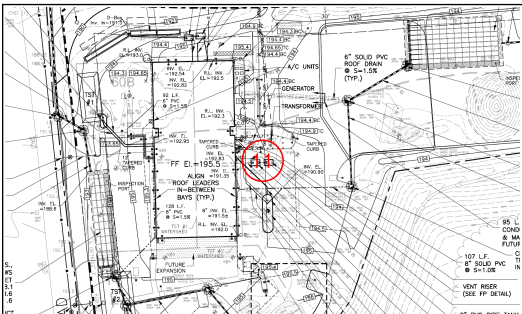

Sheet
C3

Status
Open

Created
Oct 11, 2017 at 4:14pm
mfaenza@crec.org

Last Updated
Oct 11, 2017 at 4:14pm

Description

Oil / Water Separator and Holding tanks have been installed.


North Stonington Emergency Services Building

Photos



Oct 11, 2017 at 4:14pm

#90 October 11th

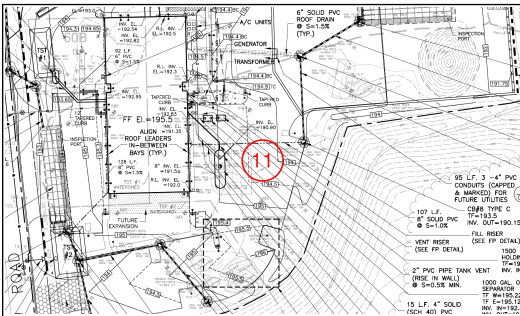

Sheet
C3

Status
Open

Created
Oct 11, 2017 at 4:13pm
mfaenza@crec.org

Last Updated
Oct 11, 2017 at 4:13pm

Description

Fire Protection storage tank has been backfilled.

Photos



Oct 11, 2017 at 4:13pm
