

North Stonington Center for Emergency Services - Field Report #17 - 11-20-17 - 11-24-17

Prepared by Michael Faenza

Description

This field report contains observations from site activities performed during the week of November 24, 2017.

The purpose of this report is to document the progress of the project.

Subcontractors working on site this week:

Suchocki & Son Inc. - Sitework

Xenelis Construction - Pre-Engineered Building

CE Electric - Electrical

Main Enterprises - Plumbing

Key Activities this week include:

Erection of Steel for Pre-Engineered Building - In Progress

Installation of Site Electrical - In Progress

Installation of gas piping and completion of associated pressure test - In progress

Installation of Fire Protection Storage Tank Cap - In Progress


Installation of Clips and Accessories for Pre-Engineered Metal Building - In Progress

Please see individual photos and locations within the report for specific detail of activities performed.

Contents

#146 November 21st	2
#147 November 21st	3
#148 November 21st	4
#149 November 21st	5
#150 November 21st	6
#151 November 22nd	7
#152 November 22nd	8
#153 November 22nd	9
#154 November 22nd	10
#155 November 22nd	11

#146 November 21st

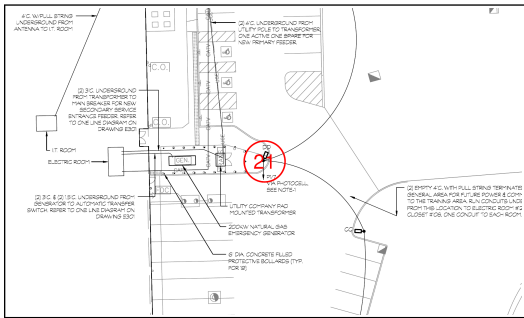

Sheet
E203

Status
Open

Created
Nov 21, 2017 at 3:36pm
mfaenza@crec.org

Last Updated
Nov 21, 2017 at 3:37pm

Description

Site lighting pole bases are being installed.


Photos



Nov 21, 2017 at 3:36pm

North Stonington Emergency Services Building

#147 November 21st

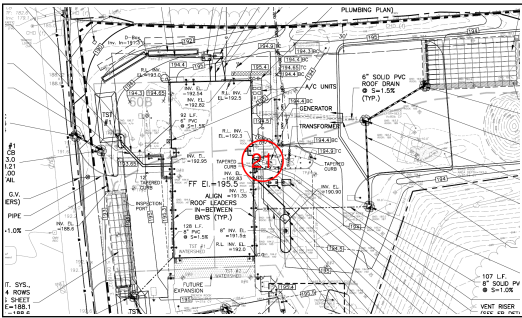

Sheet
C3

Status
Open

Created
Nov 21, 2017 at 3:37pm
mfaenza@crec.org

Last Updated
Nov 28, 2017 at 9:19am

Description


Gas piping has been brought to generator pad and a pressure test has been performed.

Photos



Nov 21, 2017 at 3:37pm

#148 November 21st

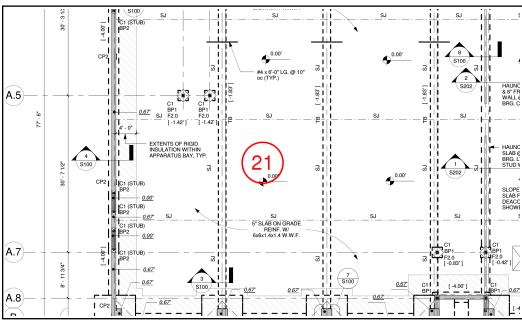

Sheet
S100

Status
Open

Created
Nov 21, 2017 at 3:38pm
mfaenza@crec.org

Last Updated
Nov 21, 2017 at 3:39pm

Description

Purlin bracing and clips are being installed in building roof system.


Photos



Nov 21, 2017 at 3:39pm

North Stonington Emergency Services Building

#149 November 21st

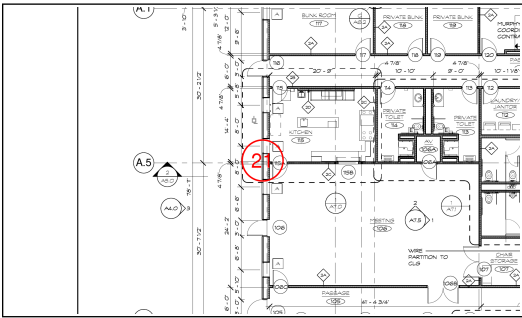

Sheet
A1.0

Status
Open

Created
Nov 21, 2017 at 3:39pm
mfaenza@crec.org

Last Updated
Nov 21, 2017 at 3:41pm

Description


Door have been installed at building administration area.

Photos



Nov 21, 2017 at 3:40pm

#150 November 21st

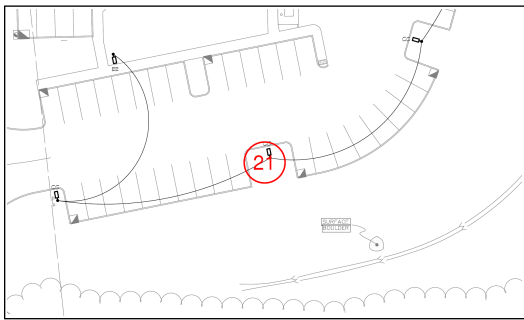

Sheet
E203

Status
Open

Created
Nov 21, 2017 at 3:41pm
mfaenza@crec.org

Last Updated
Nov 21, 2017 at 3:41pm

Description


Site lighting bases have been installed.

Photos



Nov 21, 2017 at 3:41pm

#151 November 22nd

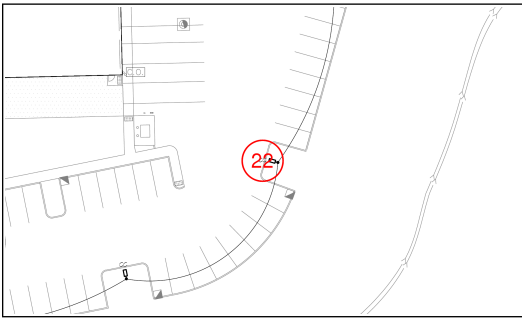

Sheet
E203

Status
Open

Created
Nov 22, 2017 at 12:30pm
mfaenza@crec.org

Last Updated
Nov 22, 2017 at 12:33pm

Description

Site lighting bases have been installed.


Photos



Nov 22, 2017 at 12:31pm

North Stonington Emergency Services Building

#152 November 22nd

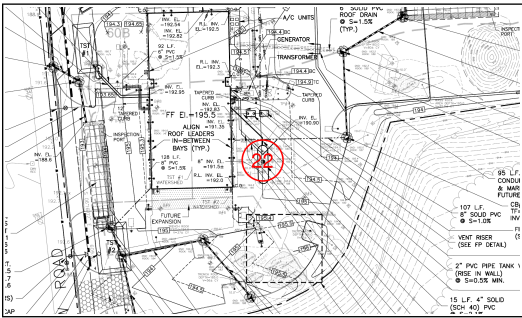

Sheet
C3

Status
Open

Created
Nov 22, 2017 at 12:34pm
mfaenza@crec.org

Last Updated
Nov 28, 2017 at 9:21am

Description


Cap has been installed and concrete pad has been installed for fire protection tank. Extension to installed once final grade is established.

Photos



Nov 22, 2017 at 12:34pm

#153 November 22nd

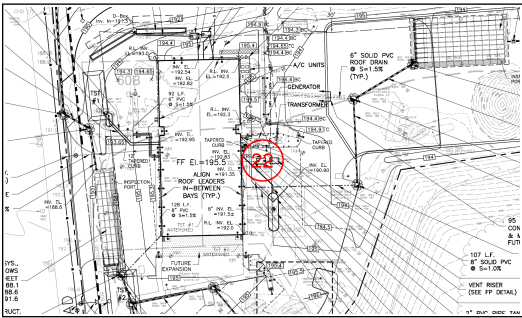

Sheet
C3

Status
Open

Created
Nov 22, 2017 at 12:35pm
mfaenza@crec.org

Last Updated
Nov 22, 2017 at 12:38pm

Description


Caps have been installed on oil water Separator tanks.

Photos



Nov 22, 2017 at 12:36pm

#154 November 22nd

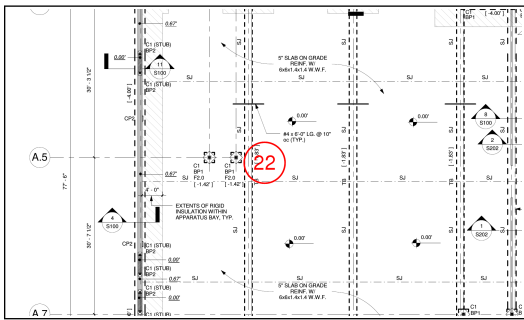

Sheet
S100

Status
Open


Created
Nov 22, 2017 at 12:38pm
mfaenza@crec.org

Last Updated
Nov 22, 2017 at 12:40pm

Description


Support braces are being installed on roof purlins.

Photos

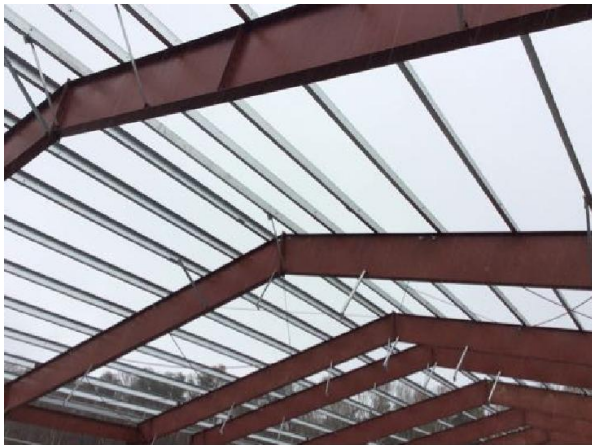

Nov 22, 2017 at 12:39pm

#155 November 22nd

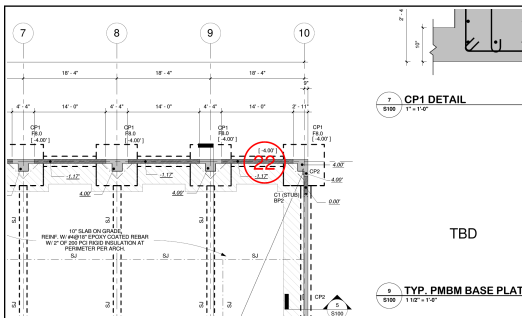

Sheet
S100

Status
Open

Created
Nov 22, 2017 at 12:40pm
mfaenza@crec.org

Last Updated
Nov 22, 2017 at 12:41pm

Description

Clips for overhead door frames are being installed.

Photos



Nov 22, 2017 at 12:41pm

North Stonington Emergency Services Building
