

North Stonington Center for Emergency Services - Field Report #22 - 1-08-18 - 1-12-18

Prepared by Michael Faenza

Description

This field report contains observations from site activities performed during the week of January 8, 2018 and January 12, 2018.

Due to the weather the project has been delayed approximately 3-4 weeks.

The purpose of this report is to document the progress of the project.

Subcontractors working on site this week:

- Xenelis Construction - Pre-Engineered Building
- MCM Acoustics LLC - Framing & Drywall
- Depco Mechanical - HVAC
- CE Electric - Electrical
- Main Enterprises - Plumbing

Key Activities this week include:

- Installation of Building Wall Panels - In Progress
- Interior Metal Framing Installation - In Progress
- Installation of Hangars for HVAC Ductwork, Fire Protection, Lighting and Plumbing in Admin Area - In Progress
- Installation of decking on Mechanical Mezzanine - Complete

Please see individual photos and locations within the report for specific detail of activities performed.


Contents

#211 January 12th	3
#210 January 12th	4
#209 January 12th	5
#208 January 12th	6
#207 January 12th	7
#206 January 10th	8

North Stonington Emergency Services Building

#205 January 10th	9
#204 January 10th	10
#203 January 10th	11
#202 January 10th	12
#201 January 10th	13
#200 January 10th	14

#211 January 12th

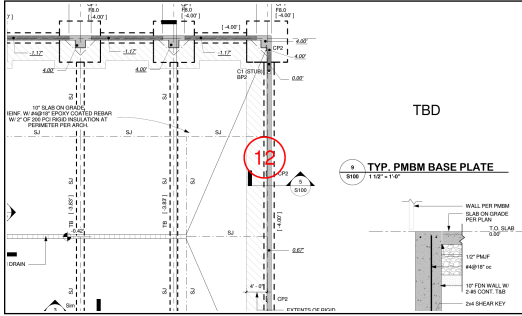

Sheet
S100

Status
Open

Assignees

Created
Jan 12, 2018 at 2:11pm
mfaenza@crec.org

Last Updated
Jan 18, 2018 at 2:15pm

Description


South building wall panel installation has been completed.

Photos



Jan 12, 2018 at 2:13pm

#210 January 12th

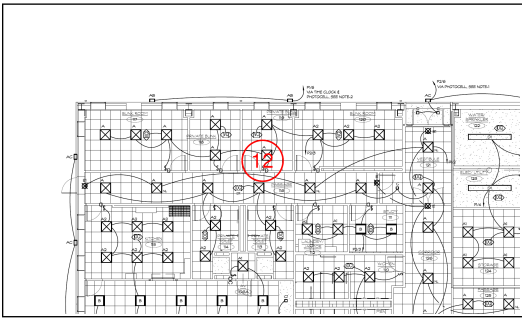

Sheet
E101

Status
Open

Assignees

Created
Jan 12, 2018 at 2:07pm
mfaenza@crec.org

Last Updated
Jan 12, 2018 at 2:11pm

Description


Temporary lighting has been installed.

Photos



Jan 12, 2018 at 2:08pm

#209 January 12th

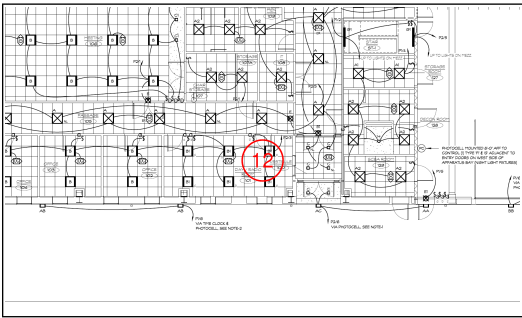

Sheet
E101

Status
Open

Assignees

Created
Jan 12, 2018 at 2:07pm
mfaenza@crec.org

Last Updated
Jan 18, 2018 at 2:15pm

Description


Cables have been installed to support interior building light fixtures.

Photos



Jan 12, 2018 at 2:07pm

#208 January 12th

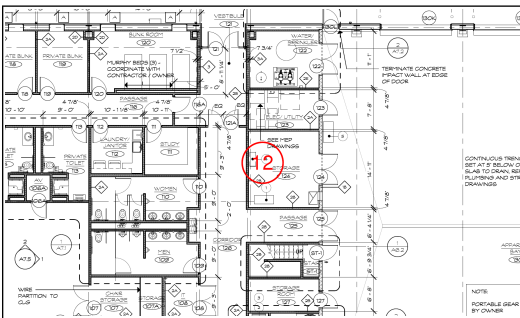

Sheet
A1.0

Status
Open

Assignees

Created
Jan 12, 2018 at 2:02pm
mfaenza@crec.org

Last Updated
Jan 18, 2018 at 2:34pm

Description

High wall framing in progress at mechanical mezzanine.


Photos



Jan 18, 2018 at 2:34pm

North Stonington Emergency Services Building

#207 January 12th

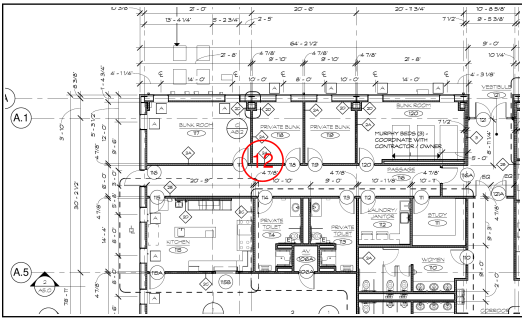

Sheet
A1.0

Status
Open

Assignees


Created
Jan 12, 2018 at 2:01pm
mfaenza@crec.org

Last Updated
Jan 12, 2018 at 2:02pm

Description

High wall has been completed at admin area.


Photos

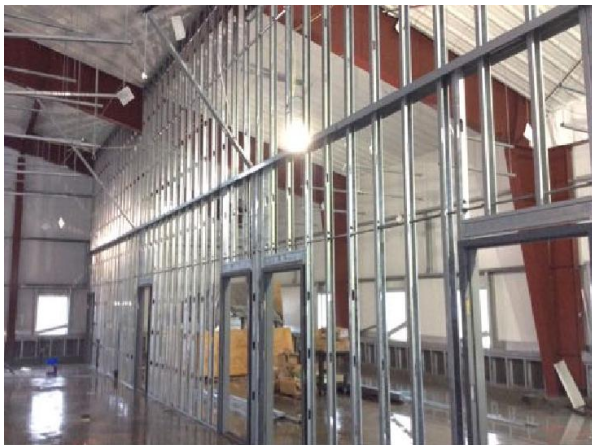

Jan 12, 2018 at 2:02pm

North Stonington Emergency Services Building

#206 January 10th

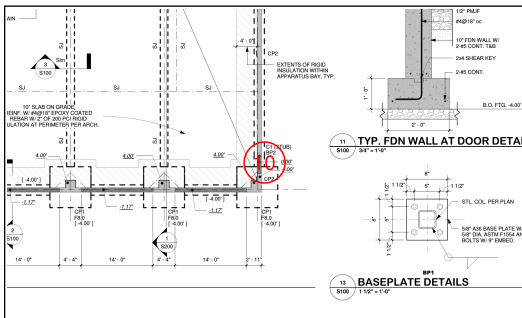

Sheet
S100

Status
Open

Assignees

Created
Jan 10, 2018 at 3:35pm
mfaenza@crec.org

Last Updated
Jan 18, 2018 at 2:13pm

Description


Metal panel installation has started on South end of building.

Photos



Jan 10, 2018 at 3:36pm

#205 January 10th

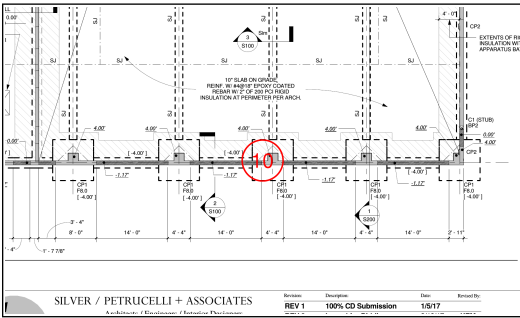

Sheet
S100

Status
Open

Assignees

Created
Jan 10, 2018 at 3:34pm
mfaenza@crec.org

Last Updated
Jan 18, 2018 at 2:14pm

Description


Metal panel installation in progress on West Side of building.

Photos



Jan 10, 2018 at 3:35pm

#204 January 10th

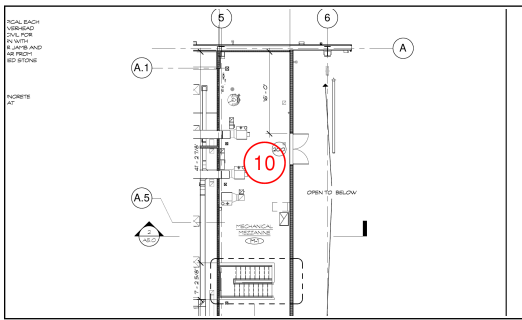

Sheet
A1.0

Status
Open

Assignees

Created
Jan 10, 2018 at 3:33pm
mfaenza@crec.org

Last Updated
Jan 10, 2018 at 3:34pm

Description


Mechanical mezzanine decking installation has been completed.

Photos



Jan 10, 2018 at 3:33pm

#203 January 10th

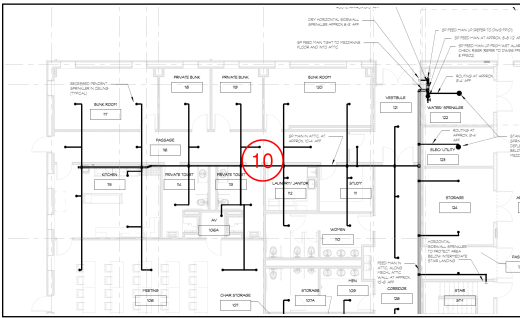

Sheet
FP101

Status
Open

Assignees


Created
Jan 10, 2018 at 3:31pm
mfaenza@crec.org

Last Updated
Jan 10, 2018 at 3:32pm

Description

Hangars for fire protection piping installation in progress.


Photos

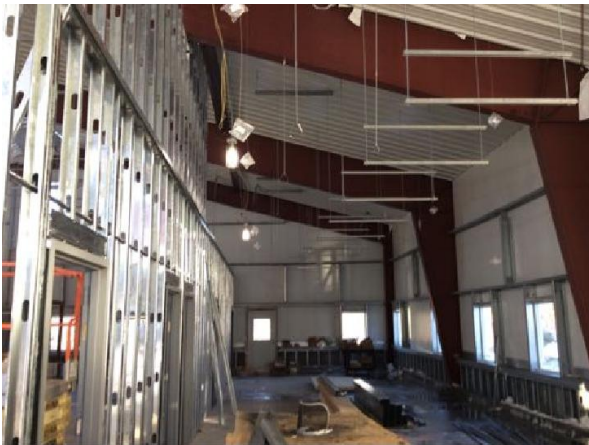

Jan 10, 2018 at 3:32pm

North Stonington Emergency Services Building

#202 January 10th

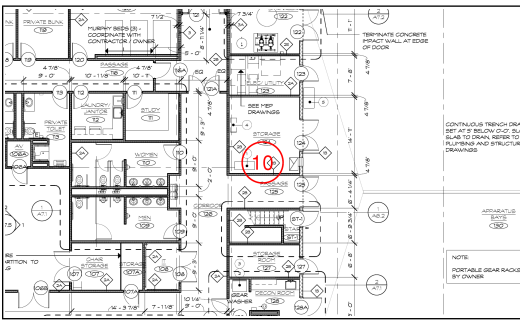

Sheet
A1.0

Status
Open

Assignees

Created
Jan 10, 2018 at 3:28pm
mfaenza@crec.org

Last Updated
Jan 10, 2018 at 3:28pm

Description

Mechanical mezzanine framing in progress.


Photos



Jan 10, 2018 at 3:28pm

North Stonington Emergency Services Building

#201 January 10th

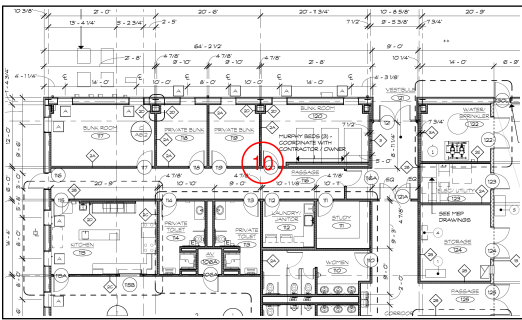

Sheet
A1.0

Status
Open

Assignees

Created
Jan 10, 2018 at 3:27pm
mfaenza@crec.org

Last Updated
Jan 10, 2018 at 3:28pm

Description

Wall framing in progress.


Photos



Jan 10, 2018 at 3:27pm

North Stonington Emergency Services Building

#200 January 10th

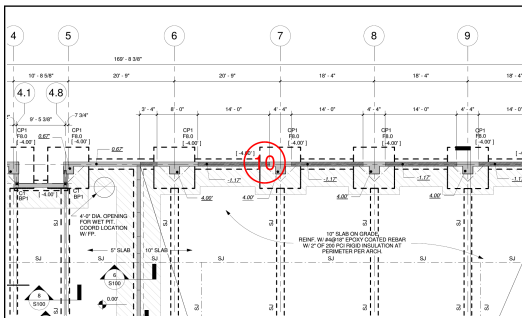

Sheet
S100

Status
Open

Assignees

Created
Jan 10, 2018 at 3:26pm
mfaenza@crec.org

Last Updated
Jan 18, 2018 at 2:13pm

Description

Metal wall panels haven't completed on East side of building.

Photos



Jan 10, 2018 at 3:26pm

North Stonington Emergency Services Building
