

North Stonington Center for Emergency Services - Field Report #12 - 10-16-17 - 10-20-17

Prepared by Michael Faenza

Description

This field report contains observations from site activities performed during the week of October 20, 2017.

The purpose of this report is to document the progress of the project.

Subcontractors working on site this week:

- Suchocki & Son Inc. - Sitework
- Black Dog Concrete - Concrete
- Main Enterprises - Plumbing
- CE Electrical - Electrical
- East Coat Wall Systems - Masonry

Key Activities this week include:

- Forming, Rebar & Mesh Installation and Pouring of Administration Area Slab - Complete
- Forming and Rebar Installation for Apparatus Bay Slab - In Progress
- Installation of Site Electrical Conduit - In Progress
- Installation of West Storm Water Management System - Complete
- Installation of Stone Veneer Mockup - In Progress

Please see individual photos and locations within the report for specific detail of activities performed.

Contents


#109 October 20th	3
#108 October 20th	3
#107 October 20th	4
#106 October 20th	5
#105 October 18th	6
#104 October 18th	7
#103 October 18th	8
#102 October 17th	9

North Stonington Emergency Services Building

#101 October 17th 10

North Stonington Emergency Services Building

#109 October 20th

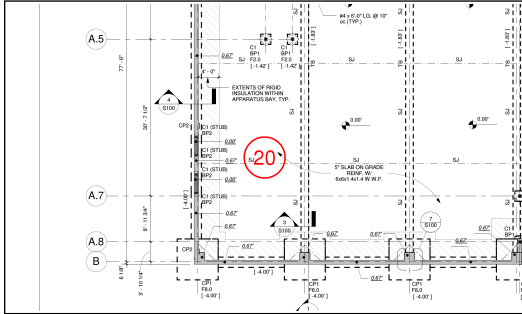

Sheet
S100

Status
Open

Created
Oct 20, 2017 at 3:53pm
mfaenza@crec.org

Last Updated
Oct 23, 2017 at 8:30am

Description


Administration area slab has been saw cut.

Photos



Oct 20, 2017 at 3:54pm

#108 October 20th

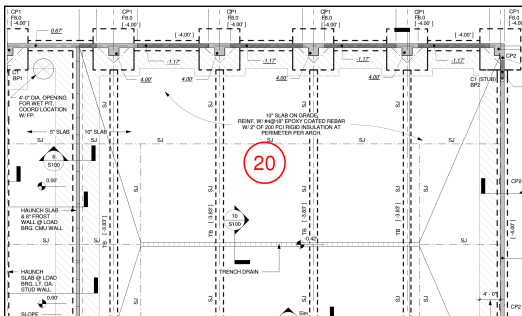

Sheet
S100

Status
Open

Created
Oct 20, 2017 at 3:52pm
mfaenza@crec.org

Last Updated
Oct 20, 2017 at 3:53pm

Description


Apparatus bay slab reinforcing installation is in progress.

Photos



Oct 20, 2017 at 3:53pm

#107 October 20th

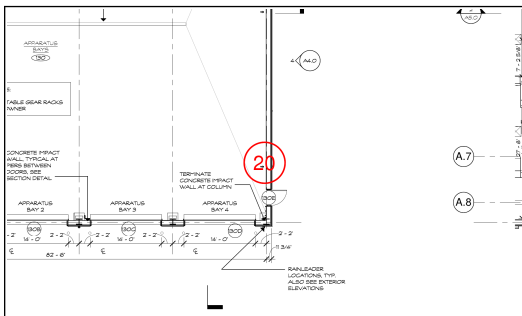

Sheet
A1.0

Status
Open

Created
Oct 20, 2017 at 3:51pm
mfaenza@crec.org

Last Updated
Oct 20, 2017 at 3:52pm

Description


Stone veneer mock is in progress of being built.

Photos



Oct 20, 2017 at 3:51pm

#106 October 20th

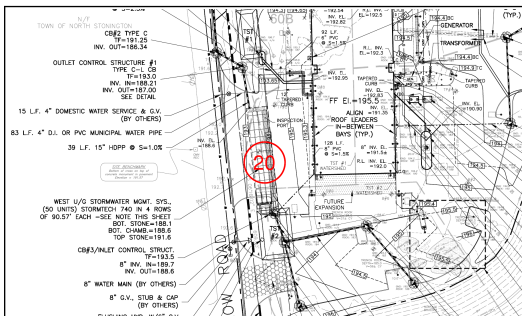

Sheet
C3

Status
Open

Created
Oct 20, 2017 at 3:50pm
mfaenza@crec.org

Last Updated
Oct 20, 2017 at 3:51pm

Description

West Stormwater management system has been backfilled.


North Stonington Emergency Services Building

Photos



Oct 20, 2017 at 3:50pm

#105 October 18th

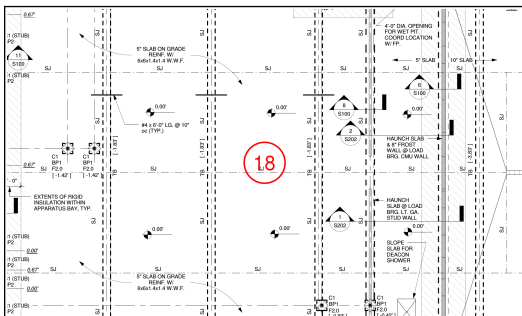

Sheet
S100

Status
Open

Created
Oct 18, 2017 at 1:13pm
mfaenza@crec.org

Last Updated
Oct 20, 2017 at 3:49pm

Description


Administration area slab is being finished.

Photos



Oct 18, 2017 at 1:13pm

#104 October 18th

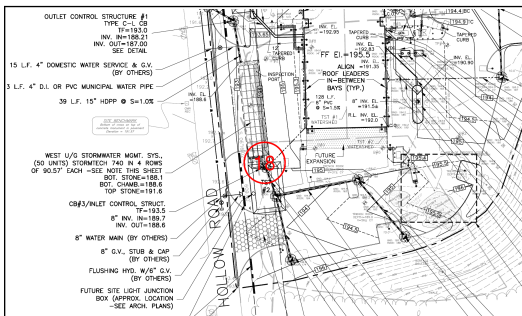

Sheet
C3

Status
Open

Created
Oct 18, 2017 at 1:09pm
mfaenza@crec.org

Last Updated
Oct 18, 2017 at 1:12pm

Description

West storm water management system has been backfilled with crushed stone and tied in.


North Stonington Emergency Services Building

Photos



Oct 18, 2017 at 1:09pm

#103 October 18th

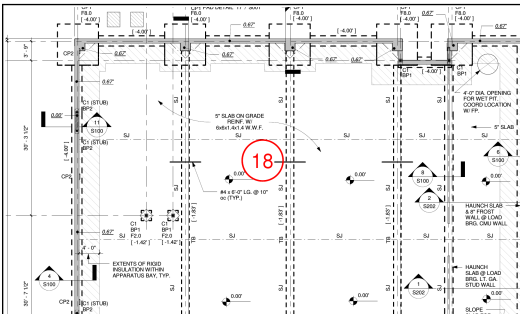

Sheet
S100

Status
Open

Created
Oct 18, 2017 at 8:45am
mfaenza@crec.org

Last Updated
Oct 18, 2017 at 8:45am

Description

Slab is being poured in administration area.


North Stonington Emergency Services Building

Photos



Oct 18, 2017 at 8:45am

#102 October 17th

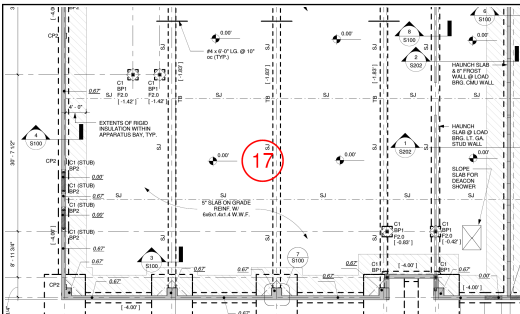

Sheet
S100

Status
Open

Created
Oct 17, 2017 at 2:52pm
mfaenza@crec.org

Last Updated
Oct 17, 2017 at 2:53pm

Description

Rebar, mesh and vapor barrier has been installed for administration area slab.


North Stonington Emergency Services Building

Photos



Oct 17, 2017 at 2:52pm

#101 October 17th

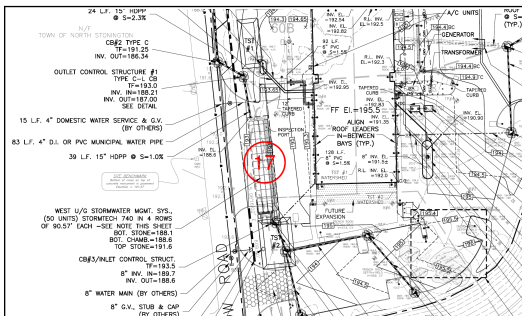

Sheet
C3

Status
Open

Created
Oct 17, 2017 at 2:50pm
mfaenza@crec.org

Last Updated
Oct 17, 2017 at 2:52pm

Description

West Stormwater management system installation in progress.

Photos



Oct 17, 2017 at 2:51pm
