

North Stonington Center for Emergency Services - Field Report #13 - 10-23-17 - 10-27-17

Prepared by Michael Faenza

Description

This field report contains observations from site activities performed during the week of October 27, 2017.

The purpose of this report is to document the progress of the project.

Subcontractors working on site this week:

- Suchocki & Son Inc. - Sitework
- Black Dog Concrete - Concrete
- Main Enterprises - Plumbing
- CE Electrical - Electrical
- East Coat Wall Systems - Masonry

Key Activities this week include:

- Forming, Rebar & Mesh Installation and Pouring of Apparatus Bay Slab - Complete
- Piping Installation for Fire Protection Tank - In Progress
- Installation of Transformer Vault - Complete
- Installation of Site Electrical Conduit - In Progress
- Installation of Grease Trap and Septic Tank - In Progress


Please see individual photos and locations within the report for specific detail of activities performed.

Contents

#110 October 23rd	3
#111 October 23rd	3
#112 October 23rd	4
#113 October 23rd	5
#114 October 25th	6
#115 October 25th	7
#116 October 25th	8
#117 October 25th	9
#118 October 27th	10

#119 October 27th 11

#110 October 23rd

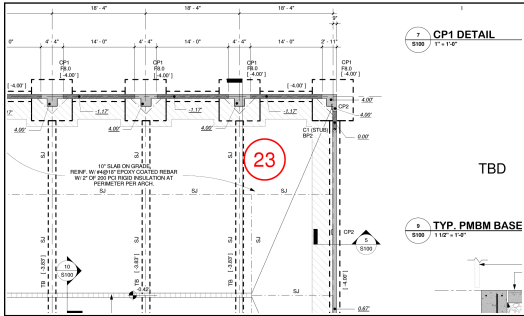

Sheet
S100

Status
Open


Created
Oct 23, 2017 at 8:30am
mfaenza@crec.org

Last Updated
Oct 23, 2017 at 8:30am

Description


Apparatus bay slab is being poured.

Photos

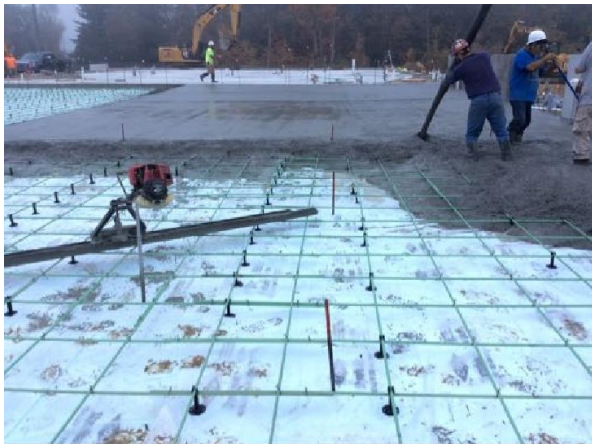

Oct 23, 2017 at 8:30am

#111 October 23rd

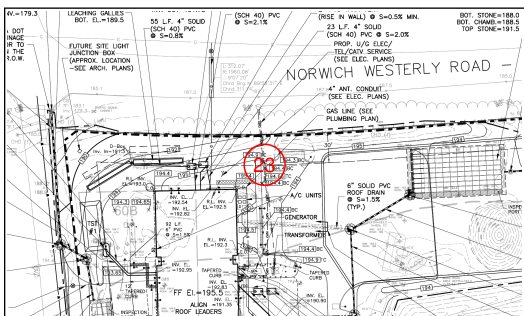

Sheet
C3

Status
Open

Created
Oct 23, 2017 at 9:14am
mfaenza@crec.org

Last Updated
Oct 23, 2017 at 9:14am

Description

Excavation in progress for utilities.


North Stonington Emergency Services Building

Photos



Oct 23, 2017 at 9:14am

#112 October 23rd

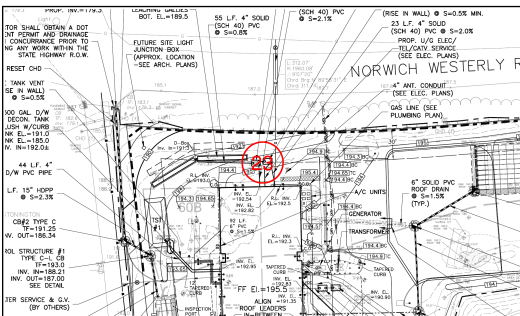

Sheet
C3

Status
Open

Created
Oct 23, 2017 at 9:15am
mfaenza@crec.org

Last Updated
Oct 23, 2017 at 10:53am

Description


Excavation in progress for grease trap and septic tank.

Photos



Oct 23, 2017 at 9:15am

#113 October 23rd

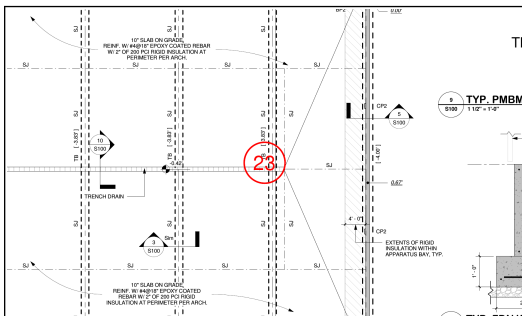

Sheet
S100

Status
Open

Created
Oct 23, 2017 at 10:53am
mfaenza@crec.org

Last Updated
Oct 25, 2017 at 3:14pm

Description

Apparatus bay slab pour is complete. Slab is being finished.


North Stonington Emergency Services Building

Photos



Oct 23, 2017 at 10:54am

#114 October 25th

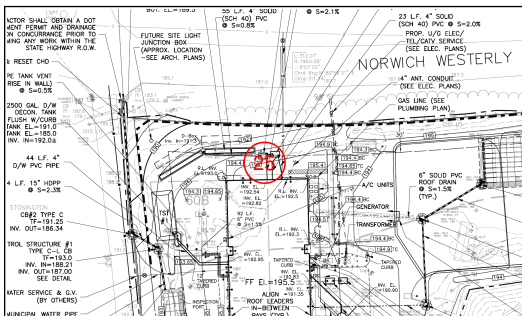

Sheet
C3

Status
Open

Created
Oct 25, 2017 at 3:15pm
mfaenza@crec.org

Last Updated
Oct 25, 2017 at 3:15pm

Description

Septic tank grease interceptor have been set.


North Stonington Emergency Services Building

Photos



Oct 25, 2017 at 3:15pm

#115 October 25th

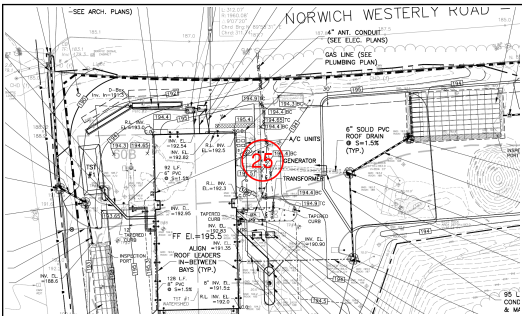

Sheet
C3

Status
Open

Created
Oct 25, 2017 at 3:16pm
mfaenza@crec.org

Last Updated
Oct 31, 2017 at 9:21am

Description

Conduit installation in progress to pole.


North Stonington Emergency Services Building

Photos



Oct 25, 2017 at 3:16pm

#116 October 25th

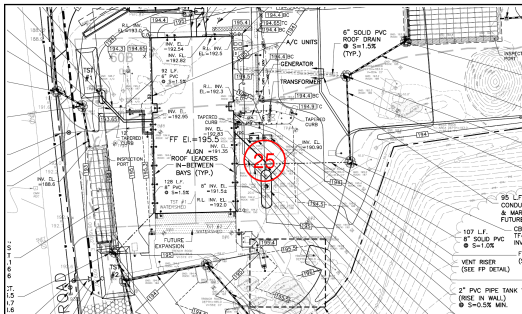

Sheet
C3

Status
Open

Created
Oct 25, 2017 at 3:18pm
mfaenza@crec.org

Last Updated
Oct 25, 2017 at 3:18pm

Description


Piping installation in progress to fire protection tank.

Photos



Oct 25, 2017 at 3:18pm

#117 October 25th

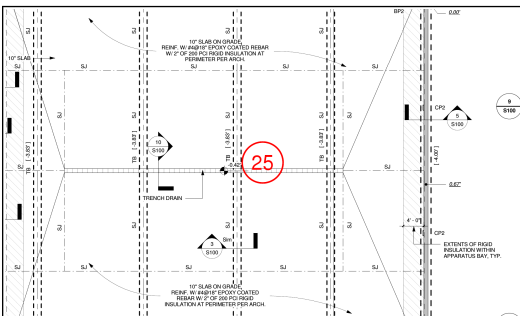

Sheet
S100

Status
Open

Created
Oct 25, 2017 at 3:19pm
mfaenza@crec.org

Last Updated
Oct 25, 2017 at 3:19pm

Description

Apparatus bay slab has been completed.


North Stonington Emergency Services Building

Photos



Oct 25, 2017 at 3:19pm

#118 October 27th

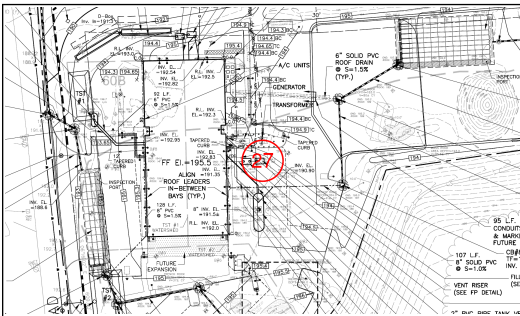

Sheet
C3

Status
Open

Created
Oct 27, 2017 at 3:17pm
mfaenza@crec.org

Last Updated
Oct 31, 2017 at 9:19am

Description

Transformer vault has been installed and conduits run into it.


North Stonington Emergency Services Building

Photos



Oct 27, 2017 at 3:17pm

#119 October 27th

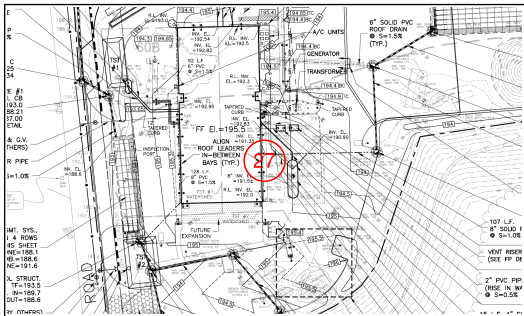

Sheet
C3

Status
Open

Created
Oct 27, 2017 at 3:18pm
mfaenza@crec.org

Last Updated
Oct 31, 2017 at 9:19am

Description

Rain leaders have been installed and stubbed up with cast iron.

Photos



Oct 27, 2017 at 3:19pm
