

North Stonington Center for Emergency Services - Field Report #16- 11-13-17 - 11-17-17

Prepared by Michael Faenza

Description

This field report contains observations from site activities performed during the week of November 17, 2017.

The purpose of this report is to document the progress of the project.

Subcontractors working on site this week:

Suchocki & Son Inc. - Sitework

Xenelis Construction - Pre-Engineered Building

CE Electric - Electric

Main Enterprises - Plumbing

Key Activities this week include:

Erection of Steel for Pre-Engineered Building - In Progress

Installation of Dumpster Pad, Generator Pad and Gas Meter Pad - Complete

Installation of Septic System - Complete

Installation of Site Electrical - In Progress

Installation and Connection of Storm Drainage to Catch Basin in Rocky Hollow Road - Complete

Please see individual photos and locations within the report for specific detail of activities performed.


Contents

#135 November 15th	3
#136 November 15th	4
#137 November 15th	5
#138 November 17th	6
#139 November 17th	7
#140 November 17th	8
#141 November 17th	9
#142 November 17th	10
#143 November 17th	11
#144 November 17th	12

#145 November 17th 13

North Stonington Emergency Services Building

#135 November 15th

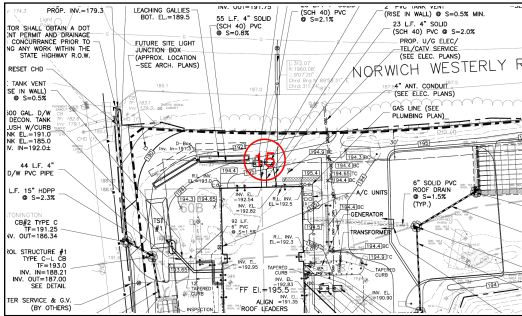

Sheet
C3

Status
Open

Created
Nov 15, 2017 at 3:39pm
mfaenza@crec.org

Last Updated
Nov 15, 2017 at 3:40pm

Description

Extensions and covers have been install on grease trap.


Photos



Nov 15, 2017 at 3:40pm

North Stonington Emergency Services Building

#136 November 15th

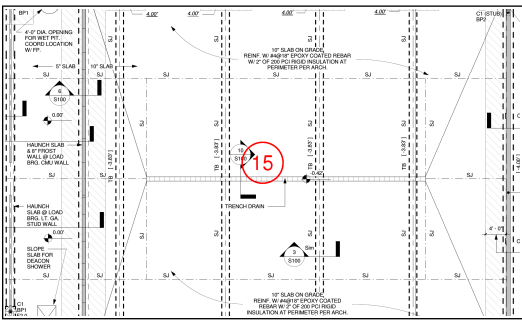

Sheet
S100

Status
Open

Created
Nov 15, 2017 at 3:41pm
mfaenza@crec.org

Last Updated
Nov 15, 2017 at 3:43pm

Description

Roof rafters have been installed.


Photos



Nov 15, 2017 at 3:41pm

North Stonington Emergency Services Building

#137 November 15th

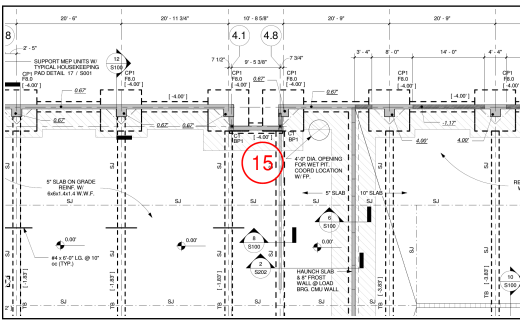

Sheet
S100

Status
Open

Created
Nov 15, 2017 at 3:44pm
mfaenza@crec.org

Last Updated
Nov 21, 2017 at 11:06am

Description

Roof purlins are being installed.


Photos



Nov 15, 2017 at 3:44pm

North Stonington Emergency Services Building

#138 November 17th

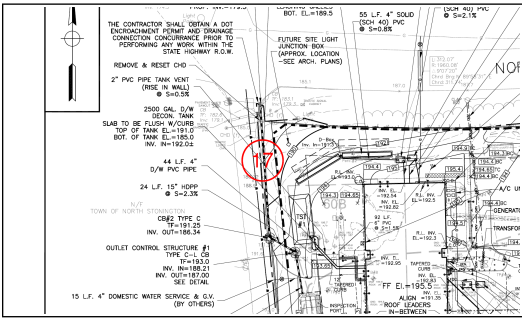

Sheet
C3

Status
Open

Created
Nov 17, 2017 at 9:26am
mfaenza@crec.org

Last Updated
Nov 17, 2017 at 9:27am

Description


Drainage piping being installed and tied to Rocky Hollow storm drainage.

Photos



Nov 17, 2017 at 9:27am

#139 November 17th

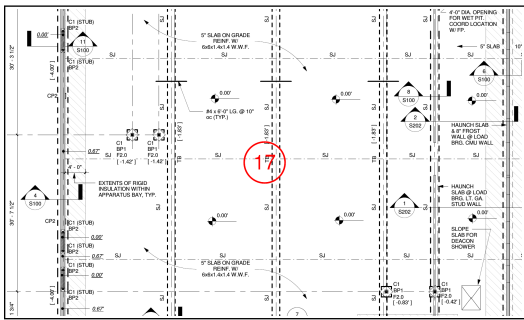

Sheet
S100

Status
Open

Created
Nov 17, 2017 at 9:27am
mfaenza@crec.org

Last Updated
Nov 17, 2017 at 9:29am

Description

Roof purlin installation in progress on administration side of building.


Photos



Nov 17, 2017 at 9:28am

North Stonington Emergency Services Building

#140 November 17th

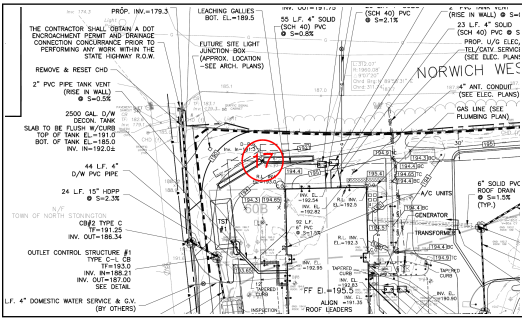

Sheet
C3

Status
Open

Created
Nov 17, 2017 at 9:29am
mfaenza@crec.org

Last Updated
Nov 17, 2017 at 9:31am

Description

Septic system installation is complete and has been inspected by Ledge Light Health District. System is awaiting back fill.

Photos




Nov 17, 2017 at 9:30am



Nov 17, 2017 at 9:31am

#141 November 17th

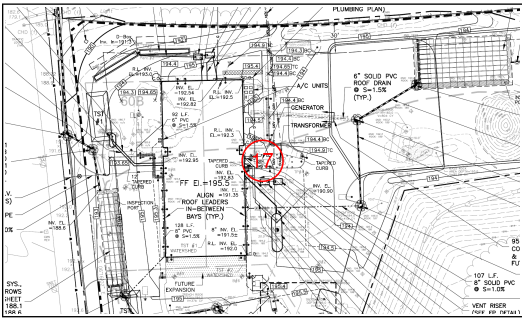

Sheet
C3

Status
Open

Created
Nov 17, 2017 at 9:32am
mfaenza@crec.org

Last Updated
Nov 17, 2017 at 9:33am

Description


Generator pad has been formed and poured.

Photos



Nov 17, 2017 at 9:33am

#142 November 17th

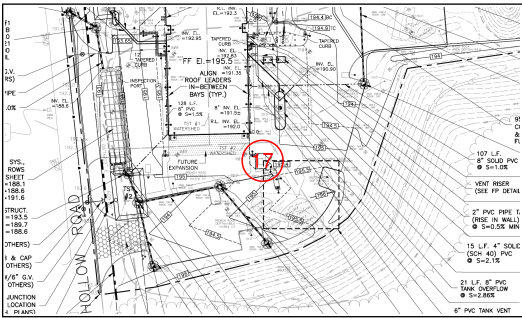

Sheet
C3

Status
Open

Created
Nov 17, 2017 at 9:33am
mfaenza@crec.org

Last Updated
Nov 17, 2017 at 9:56am

Description


Dumpster pad has been formed and poured and bollards installed.

Photos



Nov 17, 2017 at 9:34am

#143 November 17th

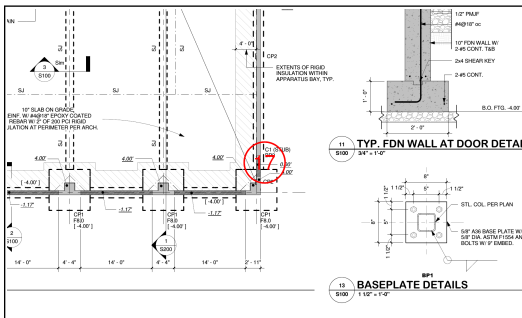

Sheet
S100

Status
Open

Created
Nov 17, 2017 at 9:56am
mfaenza@crec.org

Last Updated
Nov 17, 2017 at 9:58am

Description


Exterior man doors have been delivered.

Photos



Nov 17, 2017 at 9:57am

#144 November 17th

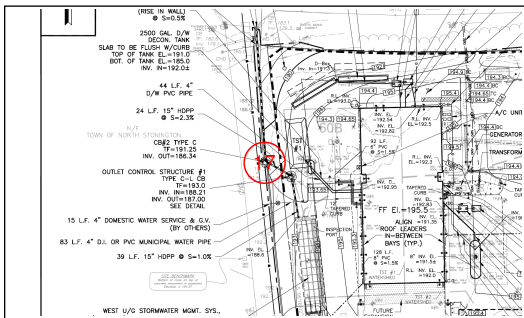

Sheet C3

Status Open

Created Nov 17, 2017 at 10:50am mfaenza@crec.org

Last Updated Nov 17, 2017 at 10:55am

Description

Excavation in progress for catch basin "CB-2"

Photos




Nov 17, 2017 at 10:51am



Nov 17, 2017 at 10:52am

#145 November 17th

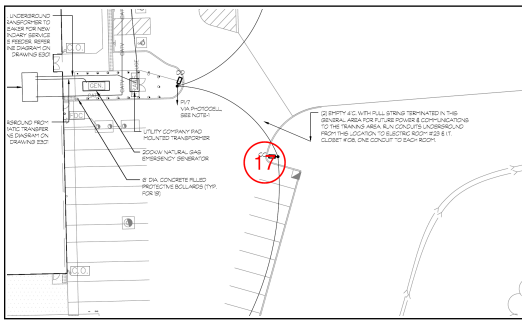

Sheet E203

Status Open

Created Nov 17, 2017 at 10:59am
mfaenza@crec.org

Last Updated Nov 17, 2017 at 11:00am

Description

Excavation for site lighting in progress.

Photos



Nov 17, 2017 at 11:00am

North Stonington Emergency Services Building
