

North Stonington Center for Emergency Services - Field Report #5 - 8-28-17 - 9-1-17

Prepared by Michael Faenza

Description

This field report contains observations from site activities performed during the week of September 1, 2017.

The purpose of this report is to document the progress of the project.

Subcontractors working on site this week:

Suchocki & Son Inc. - Sitework

Black Dog Concrete - Concrete

Key Activities this week include:

Installation of Rebar for Concrete Footings - In Progress

Placement of Concrete for Building Footing - In Progress

Excavation and Installation for Wet Well and associated piping - In Progress


Please see individual photos and locations within the report for specific detail of activities performed.

Contents

#31 August 29th	2
#32 August 29th	2
#33 August 29th	3
#34 August 30th	4
#35 August 30th	5
#36 August 30th	6
#37 August 31st	7
#38 August 31st	8

North Stonington Emergency Services Building

#31 August 29th

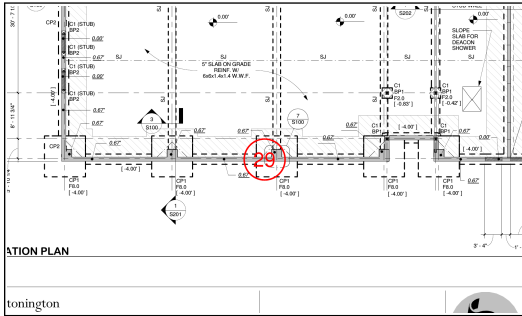

Sheet
S100

Status
Open

Created
Aug 29, 2017 at 2:16pm
mfaenza@crec.org

Last Updated
Aug 29, 2017 at 2:18pm

Description


Rebar for footings and piers is being installed.

Photos



Aug 29, 2017 at 2:17pm

#32 August 29th

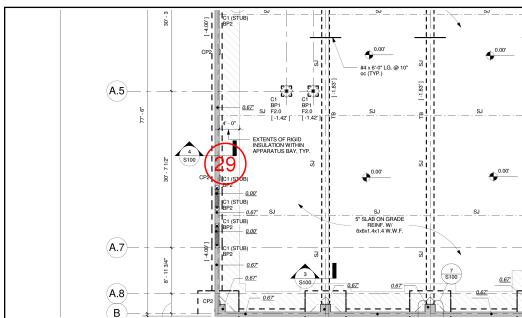

Sheet
S100

Status
Open

Created
Aug 29, 2017 at 2:18pm
mfaenza@crec.org

Last Updated
Aug 29, 2017 at 2:19pm

Description


Rebar for footings and piers is being installed.

Photos



Aug 29, 2017 at 2:19pm

#33 August 29th

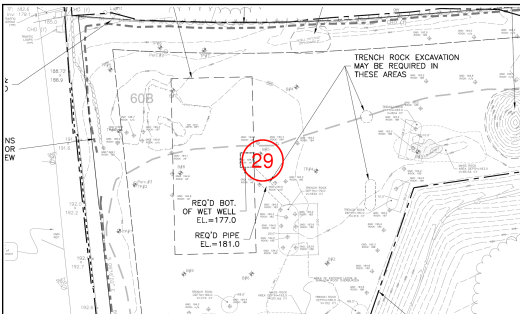

Sheet
C2

Status
Open

Created
Aug 29, 2017 at 2:19pm
mfaenza@crec.org

Last Updated
Aug 29, 2017 at 2:23pm

Description

Excavation has been increased for wet well. Trench box has been placed until wet well is delivered. Trench for wet well piping is being excavated.


North Stonington Emergency Services Building

Photos



Aug 29, 2017 at 2:20pm

#34 August 30th

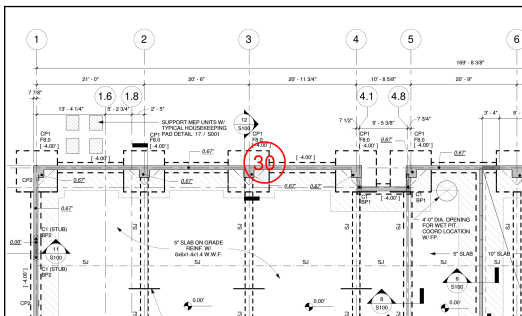

Sheet
S100

Status
Open

Created
Aug 30, 2017 at 2:12pm
mfaenza@crec.org

Last Updated
Aug 30, 2017 at 2:16pm

Description

Concrete is being placed.


North Stonington Emergency Services Building

Photos



Aug 30, 2017 at 2:12pm

#35 August 30th

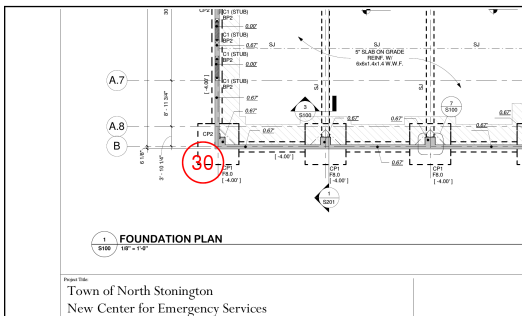

Sheet
S100

Status
Open

Created
Aug 30, 2017 at 3:05pm
mfaenza@crec.org

Last Updated
Aug 30, 2017 at 3:25pm

Description


Concrete being placed.

Photos



Aug 30, 2017 at 3:05pm

#36 August 30th

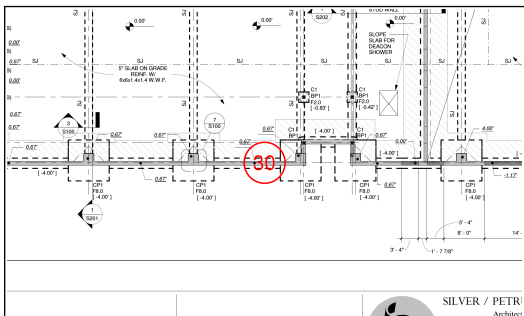

Sheet
S100

Status
Open

Created
Aug 30, 2017 at 3:25pm
mfaenza@crec.org

Last Updated
Aug 30, 2017 at 3:26pm

Description

Concrete is being placed.


North Stonington Emergency Services Building

Photos



Aug 30, 2017 at 3:26pm

#37 August 31st

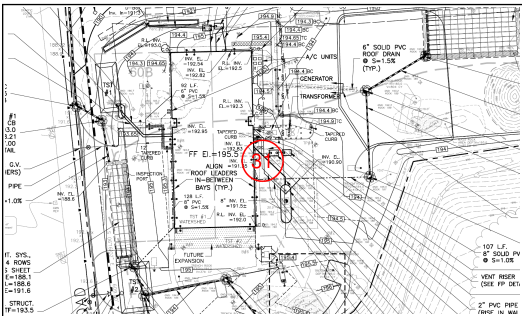

Sheet
C3

Status
Open

Created
Aug 31, 2017 at 12:27pm
mfaenza@crec.org

Last Updated
Aug 31, 2017 at 12:27pm

Description


Wet well piping is being installed.

Photos



Aug 31, 2017 at 12:27pm

#38 August 31st

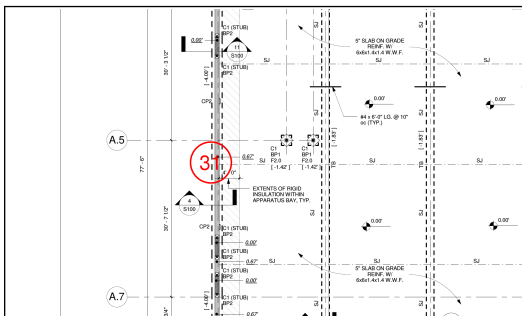

Sheet
S100

Status
Open

Created
Aug 31, 2017 at 12:28pm
mfaenza@crec.org

Last Updated
Aug 31, 2017 at 12:28pm

Description

Footing formwork has been striped.

Photos



Aug 31, 2017 at 12:28pm
