

North Stonington Center for Emergency Services - Field Report #8 - 9-18-17 - 9-22-17

Prepared by Michael Faenza

Description

This field report contains observations from site activities performed during the week of September 22, 2017.

The purpose of this report is to document the progress of the project.

Subcontractors working on site this week:

- Suchocki & Son Inc. - Sitework
- Black Dog Concrete - Concrete
- Main Enterprises - Plumbing

Key Activities this week include:

- Installation of Fire Protection Wet Well Structure - Complete
- Backfill of Wet Well Excavation - In Progress
- Installation of Storm Water Management System - In Progress
- Forming and Pouring of Tie, Beams, Foundation Walls and Impact Walls - In Progress
- Installation of Underground Sanitary and Grease Waste Piping - In Progress


Please see individual photos and locations within the report for specific detail of activities performed.

Contents

#53 September 19th	3
#54 September 19th	3
#55 September 19th	4
#56 September 20th	5
#57 September 20th	6
#58 September 21st	7
#59 September 21st	8
#60 September 21st	9
#61 September 21st	10
#62 September 21st	11

#63 September 21st 12

#53 September 19th

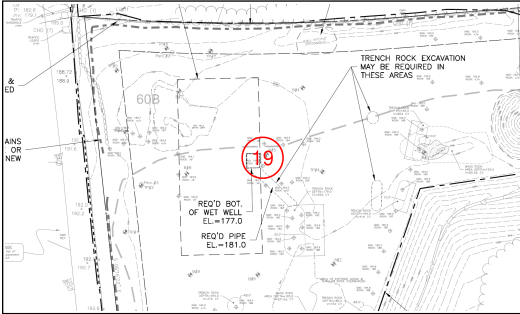

Sheet
C2

Status
Open

Created
Sep 19, 2017 at 10:02am
mfaenza@crec.org

Last Updated
Sep 19, 2017 at 3:15pm

Description


Wet well has arrived and been dropped into pit.

Photos



Sep 19, 2017 at 10:02am

#54 September 19th

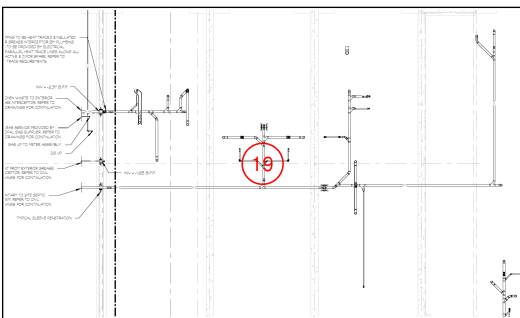

Sheet
P100

Status
Open

Created
Sep 19, 2017 at 3:15pm
mfaenza@crec.org

Last Updated
Sep 19, 2017 at 3:16pm

Description

Underground plumbing installation has commenced.


North Stonington Emergency Services Building

Photos



Sep 19, 2017 at 3:16pm

#55 September 19th

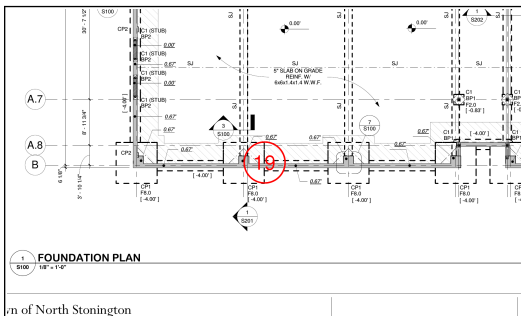

Sheet
S100

Status
Open

Created
Sep 19, 2017 at 3:17pm
mfaenza@crec.org

Last Updated
Sep 19, 2017 at 3:19pm

Description


Foundation wall has been backfilled.

Photos



Sep 19, 2017 at 3:18pm

#56 September 20th

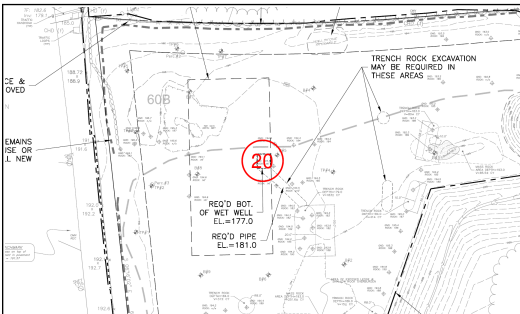

Sheet
C2

Status
Open

Created
Sep 20, 2017 at 3:13pm
mfaenza@crec.org

Last Updated
Sep 20, 2017 at 3:15pm

Description

Wet well has been connected and is being tested with water.

Photos




Sep 20, 2017 at 3:14pm



Sep 20, 2017 at 3:14pm

#57 September 20th

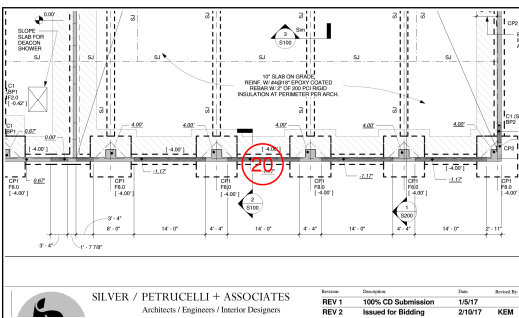

Sheet
S100

Status
Open

Created
Sep 20, 2017 at 3:16pm
mfaenza@crec.org

Last Updated
Sep 21, 2017 at 2:58pm

Description

Foundation walls and piers have been formed at apparatus bay doors.


North Stonington Emergency Services Building

Photos



Sep 20, 2017 at 3:16pm

#58 September 21st

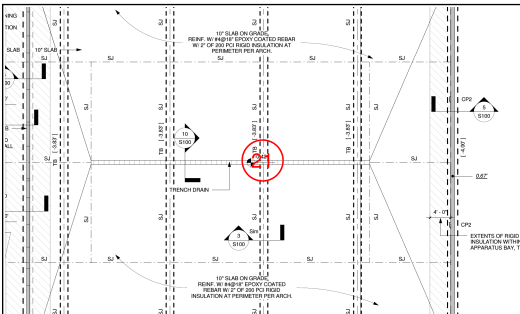

Sheet
S100

Status
Open

Created
Sep 21, 2017 at 2:58pm
mfaenza@crec.org

Last Updated
Sep 21, 2017 at 2:59pm

Description

Tie beams have been poured.


North Stonington Emergency Services Building

Photos



Sep 21, 2017 at 2:59pm

#59 September 21st

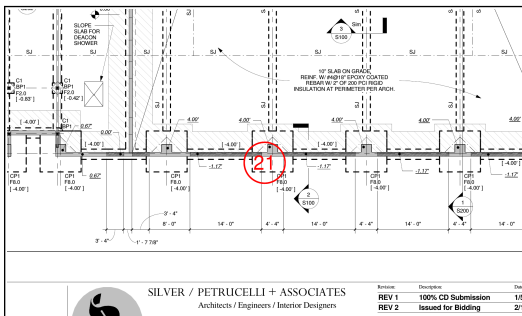

Sheet
S100

Status
Open

Created
Sep 21, 2017 at 2:59pm
mfaenza@crec.org

Last Updated
Sep 21, 2017 at 3:00pm

Description


Foundation wall and impact walls have been poured.

Photos



Sep 21, 2017 at 2:59pm

#60 September 21st

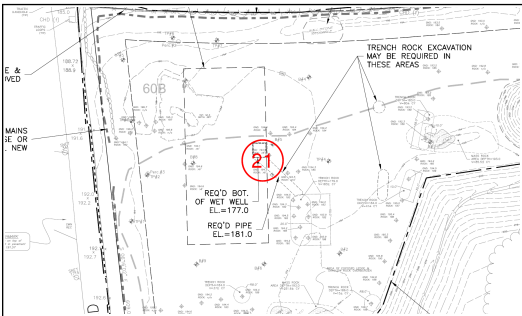

Sheet
C2

Status
Open

Created
Sep 21, 2017 at 3:00pm
mfaenza@crec.org

Last Updated
Sep 21, 2017 at 3:02pm

Description

Wet well has been partially back-filled.


North Stonington Emergency Services Building

Photos



Sep 21, 2017 at 3:01pm

#61 September 21st

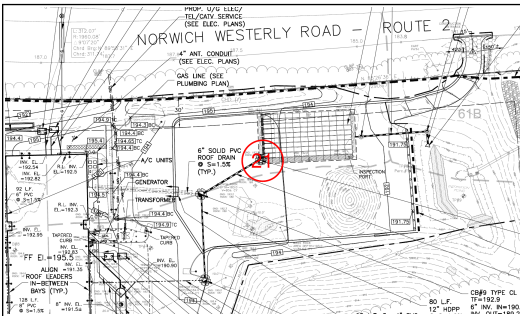

Sheet
C3

Status
Open

Created
Sep 21, 2017 at 3:02pm
mfaenza@crec.org

Last Updated
Sep 21, 2017 at 3:03pm

Description


Stormwater inlet structure has been installed and tied into Stormwater management system.

Photos



Sep 21, 2017 at 3:03pm

#62 September 21st

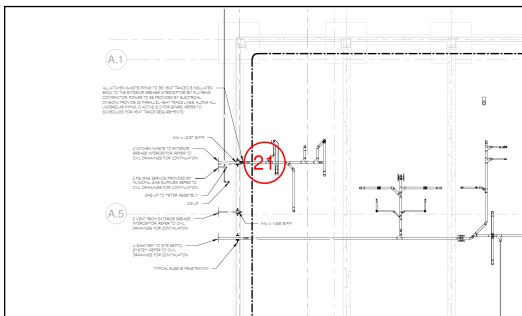

Sheet
P100

Status
Open

Created
Sep 21, 2017 at 3:05pm
mfaenza@crec.org

Last Updated
Sep 21, 2017 at 3:05pm

Description


Grease interceptor piping in progress.

Photos



Sep 21, 2017 at 3:05pm

#63 September 21st

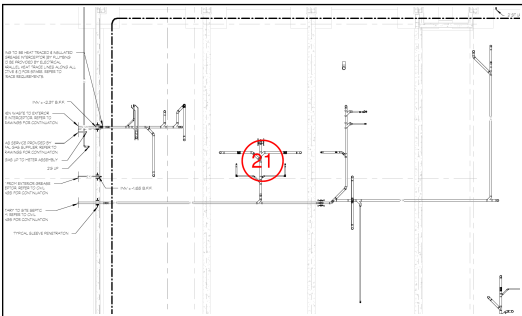

Sheet
P100

Status
Open

Created
Sep 21, 2017 at 3:06pm
mfaenza@crec.org

Last Updated
Sep 21, 2017 at 3:06pm

Description

Underground piping has been stubbed up.

Photos



Sep 21, 2017 at 3:06pm
