

North Stonington Center for Emergency Services - Field Report #9 - 9-25-17 - 9-29-17

Prepared by Michael Faenza

Description

This field report contains observations from site activities performed during the week of September 29, 2017.

The purpose of this report is to document the progress of the project.

Subcontractors working on site this week:

- Suchocki & Son Inc. - Sitework
- Black Dog Concrete - Concrete
- Main Enterprises - Plumbing

Key Activities this week include:

- Excavation for Fire Protection Storage Tank - Complete
- Backfill of Storm Water Management System - In Progress
- Forming and Pouring of Tie, Beams, Foundation Walls and Impact Walls - In Progress
- Installation of Underground Sanitary and Grease Waste Piping - In Progress
- Installation of Roof Leader Drainage Piping - In Progress
- Backfilling of Building Interior Slabs - In Progress

Please see individual photos and locations within the report for specific detail of activities performed.


Contents

#64 September 26th	3
#65 September 26th	3
#66 September 26th	4
#67 September 26th	5
#68 September 26th	6
#69 September 27th	7
#70 September 27th	8
#71 September 27th	9
#72 September 27th	10
#73 September 29th	11

North Stonington Emergency Services Building

#74 September 29th	12
#75 September 29th	13
#76 September 29th	14
#77 September 29th	15

#64 September 26th

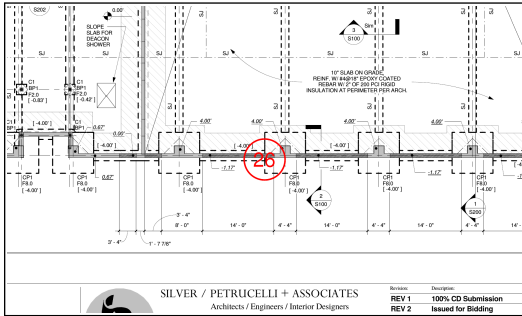

Sheet S100

Status Open

Created Sep 26, 2017 at 9:25am mfaenza@crec.org

Last Updated Sep 26, 2017 at 9:26am

Description


Impact walls at apparatus bays have been poured and stripped.

Photos



Sep 26, 2017 at 9:25am

#65 September 26th

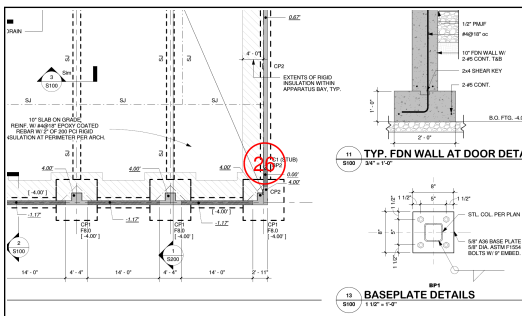

Sheet S100

Status Open

Created Sep 26, 2017 at 9:26am mfaenza@crec.org

Last Updated Sep 26, 2017 at 9:27am

Description

Foundation wall has been formed and rebar installed.


North Stonington Emergency Services Building

Photos



Sep 26, 2017 at 9:26am

#66 September 26th

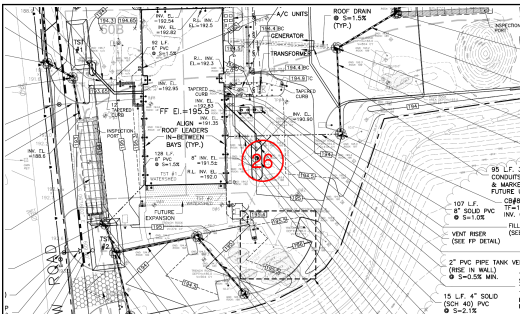

Sheet
C3

Status
Open

Created
Sep 26, 2017 at 9:27am
mfaenza@crec.org

Last Updated
Sep 26, 2017 at 9:28am

Description

Excavation for 20,000 gallon fire protection tank has commenced.


North Stonington Emergency Services Building

Photos



Sep 26, 2017 at 9:27am

#67 September 26th

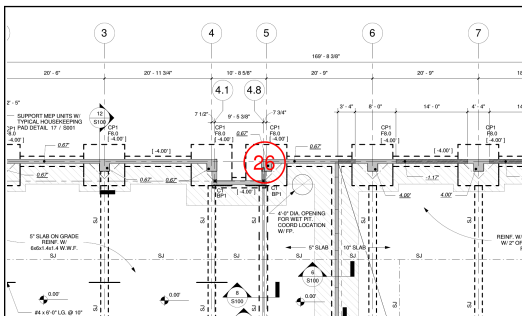

Sheet
S100

Status
Open

Created

Sep 26, 2017 at 9:28am
mfaenza@crec.org

Last Updated

Sep 26, 2017 at 9:29am

Description

Layout and installation of balance of concrete footings near wet well is in progress.


North Stonington Emergency Services Building

Photos



Sep 26, 2017 at 9:29am

#68 September 26th

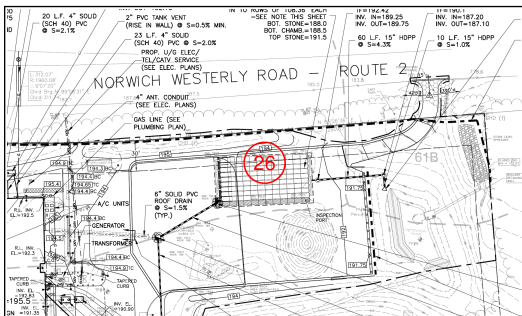

Sheet
C3

Status
Open

Created
Sep 26, 2017 at 9:30am
mfaenza@crec.org

Last Updated
Sep 27, 2017 at 3:05pm

Description

Stormwater interceptor has been filled with stone. Sitework contractor has placed geo-fabric and is placing fill on top of system.


North Stonington Emergency Services Building

Photos



Sep 26, 2017 at 9:31am

#69 September 27th

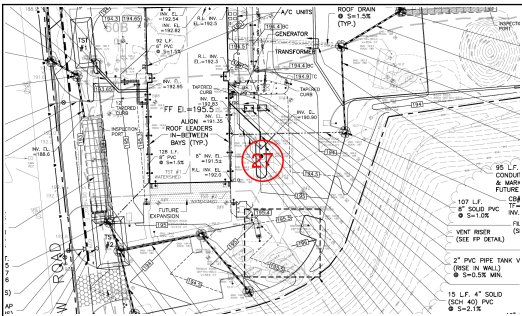

Sheet
C3

Status
Open

Created
Sep 27, 2017 at 3:05pm
mfaenza@crec.org

Last Updated
Sep 27, 2017 at 3:06pm

Description


Fire protection tank excavation has been completed.

Photos



Sep 27, 2017 at 3:06pm

#70 September 27th

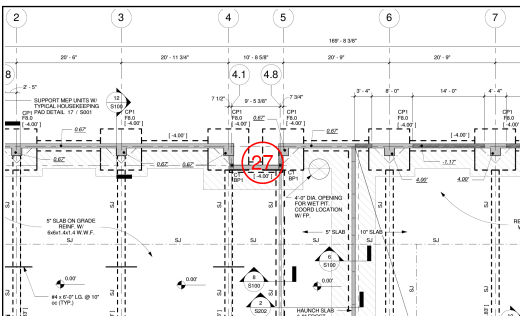

Sheet
S100

Status
Open

Created
Sep 27, 2017 at 3:09pm
mfaenza@crec.org

Last Updated
Sep 27, 2017 at 3:09pm

Description

Concrete footing has been poured.


North Stonington Emergency Services Building

Photos



Sep 27, 2017 at 3:09pm

#71 September 27th

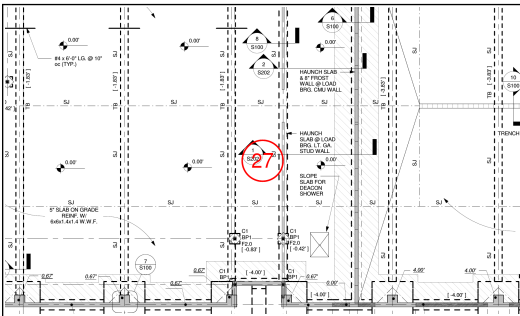

Sheet
S100

Status
Open

Created
Sep 27, 2017 at 3:09pm
mfaenza@crec.org

Last Updated
Sep 27, 2017 at 3:10pm

Description

Tie beams have been poured.


North Stonington Emergency Services Building

Photos



Sep 27, 2017 at 3:09pm

#72 September 27th

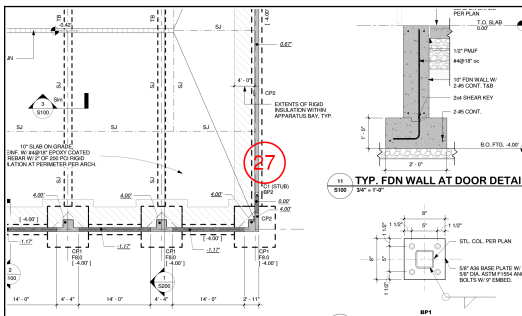

Sheet
S100

Status
Open

Created
Sep 27, 2017 at 3:10pm
mfaenza@crec.org

Last Updated
Sep 29, 2017 at 1:51pm

Description


Concrete foundation wall and apparatus bay impact walls have been poured.

Photos



Sep 27, 2017 at 3:11pm

#73 September 29th

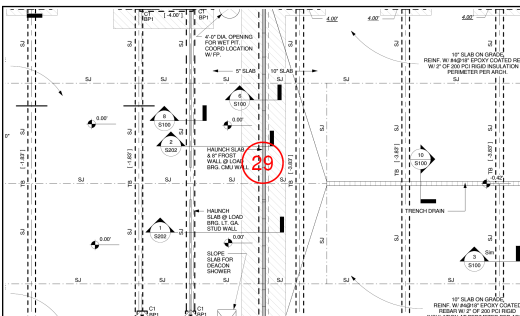

Sheet
S100

Status
Open

Created
Sep 29, 2017 at 1:52pm
mfaenza@crec.org

Last Updated
Sep 29, 2017 at 1:53pm

Description


Concrete wall has been poured between apparatus bay and administration area.

Photos



Sep 29, 2017 at 1:52pm

#74 September 29th

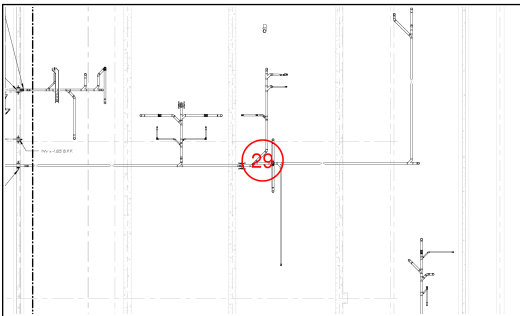

Sheet
P100

Status
Open

Created
Sep 29, 2017 at 1:54pm
mfaenza@crec.org

Last Updated
Sep 29, 2017 at 1:55pm

Description

Underground piping has been installed.


North Stonington Emergency Services Building

Photos



Sep 29, 2017 at 1:55pm

#75 September 29th

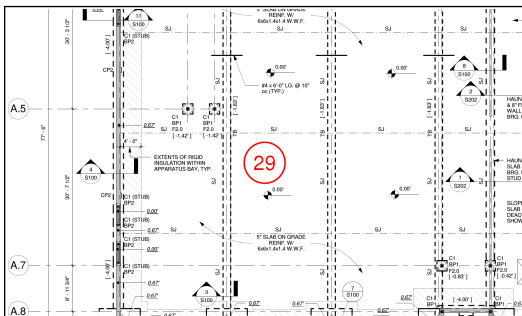

Sheet
S100

Status
Open

Created
Sep 29, 2017 at 1:55pm
mfaenza@crec.org

Last Updated
Sep 29, 2017 at 1:56pm

Description

Backfill is in progress in administration area.


North Stonington Emergency Services Building

Photos



Sep 29, 2017 at 1:56pm

#76 September 29th

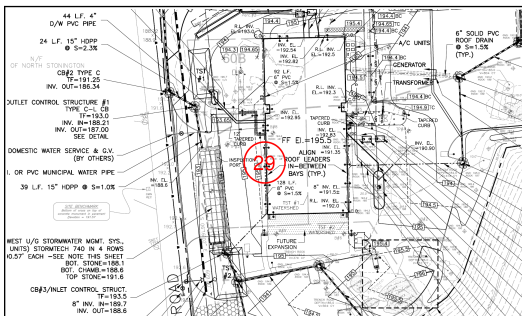

Sheet
C3

Status
Open

Created
Sep 29, 2017 at 1:56pm
mfaenza@crec.org

Last Updated
Sep 29, 2017 at 1:57pm

Description


Installation of building roof rain water leader drainage piping has begun.

Photos



Sep 29, 2017 at 1:57pm

#77 September 29th

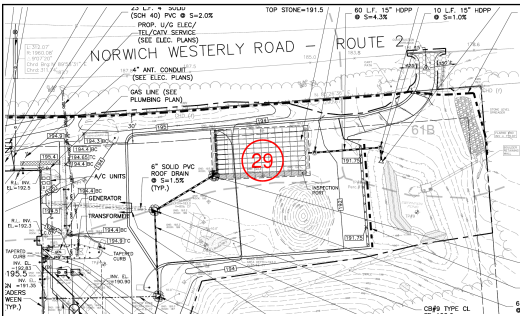

Sheet
C3

Status
Open

Created
Sep 29, 2017 at 1:59pm
mfaenza@crec.org

Last Updated
Sep 29, 2017 at 2:29pm

Description

Stormwater management system has been inspected by the manufacturer and back fill is in progress.

Photos



Sep 29, 2017 at 1:59pm
